























	Naam	Duur	Begin	Einde	Deadline	Voorgangers
1		Technische oplevering ...	50 dagen?	1-12-20 8:00	8-2-21 17:00	11-2-21 17:00	
2		Installatie GMS op accep...	1 dag?	1-12-20 8:00	1-12-20 17:00		
3		FAT	1 dag?	3-12-20 8:00	3-12-20 17:00		2
4		GAT plan gereed	4 dagen	1-12-20 8:00	4-12-20 17:00		
5		Pilotplan schrijven	5 dagen	1-12-20 8:00	7-12-20 17:00	10-12-20 17:00	
6		Schrijven plan pre imple...	5 dagen	1-12-20 8:00	7-12-20 17:00		
7		Monitoren aanpassingen...	4 dagen	4-12-20 8:00	9-12-20 17:00		3
8		Go no go GAT	0 dagen	9-12-20 8:00	9-12-20 8:00		4
9		GAT	1 dag?	10-12-20 8:00	10-12-20 17:00		8
10		Monitoren aanpassingen...	4 dagen	11-12-20 8:00	16-12-20 17:00	16-12-20 17:00	9
11		Informeren stakeholders...	1 dag?	11-12-20 8:00	11-12-20 17:00	11-12-20 17:00	9;5
12		Go/No Go Pilot	0 dagen	16-12-20 8:00	16-12-20 8:00	16-12-20 17:00	
13		Pilot	1 dag?	17-12-20 8:00	17-12-20 17:00		12
14		Oplossen bevindingen	5 dagen	18-12-20 8:00	24-12-20 17:00		13
15		Technisch gereed maken...	5 dagen	4-1-21 8:00	8-1-21 17:00		
16		Installeren GMS op prod...	1 dag?	11-1-21 8:00	11-1-21 17:00	11-1-21 17:00	
17		Installeren KPN BR 3 Pro...	1 dag?	11-1-21 8:00	11-1-21 17:00	11-1-21 17:00	
18		Doorvoeren lokale instelli...	1 dag?	12-1-21 8:00	12-1-21 17:00		16
19		Pre-implementatietest	1 dag?	13-1-21 8:00	13-1-21 17:00		6;18
20		Bevindingen aanpassen	1 dag	14-1-21 8:00	14-1-21 17:00	15-1-21 17:00	19
21		Go/No Go Pilot	0 dagen	14-1-21 17:00	14-1-21 17:00	15-1-21 17:00	20
22		Pilot	1 dag?	18-1-21 8:00	18-1-21 17:00		
23		Doorvoeren laatste aan...	1 dag?	19-1-21 8:00	19-1-21 17:00	4-2-21 17:00	22
24		Go no go Livegang	0 dagen	4-2-21 17:00	4-2-21 17:00		23
25		Finale check	1 dag?	8-2-21 8:00	8-2-21 17:00		
26		Inrichten meldkamers	13 dagen?	1-12-20 8:00	17-12-20 17:00		
27		Meldkamer instellingen B...	5 dagen	1-12-20 8:00	7-12-20 17:00	10-12-20 17:00	
28		Migratieplan meldkamers	5 dagen	8-12-20 8:00	14-12-20 17:00	10-12-20 17:00	27
29		Informeren lokaal beheer...	1 dag?	17-12-20 8:00	17-12-20 17:00	1-12-20 17:00	28
30		Inrichten beheer	35 dagen?	1-12-20 8:00	18-1-21 17:00		
31		Beheerprocessen ingericht	15 dagen	1-12-20 8:00	21-12-20 17:00	18-12-20 17:00	
32		ORT	1 dag?	28-12-20 8:00	28-12-20 17:00	18-1-21 17:00	31
33		Start informeren MMC e...	15 dagen	29-12-20 8:00	18-1-21 17:00		32
34		Training	1 dag?	1-12-20 8:00	1-12-20 17:00		



25 jan 21					1 feb 21					8 feb 21					15 feb 21					22 feb 21					1 mrt 21					8 mrt 21																
M	D	W	D	V	Z	Z	M	D	W	D	V	Z	Z	M	D	W	D	V	Z	Z	M	D	W	D	V	Z	Z	M	D	W	D	V	Z	Z	M	D	W	D	V	Z	Z	M	D	W	D	V

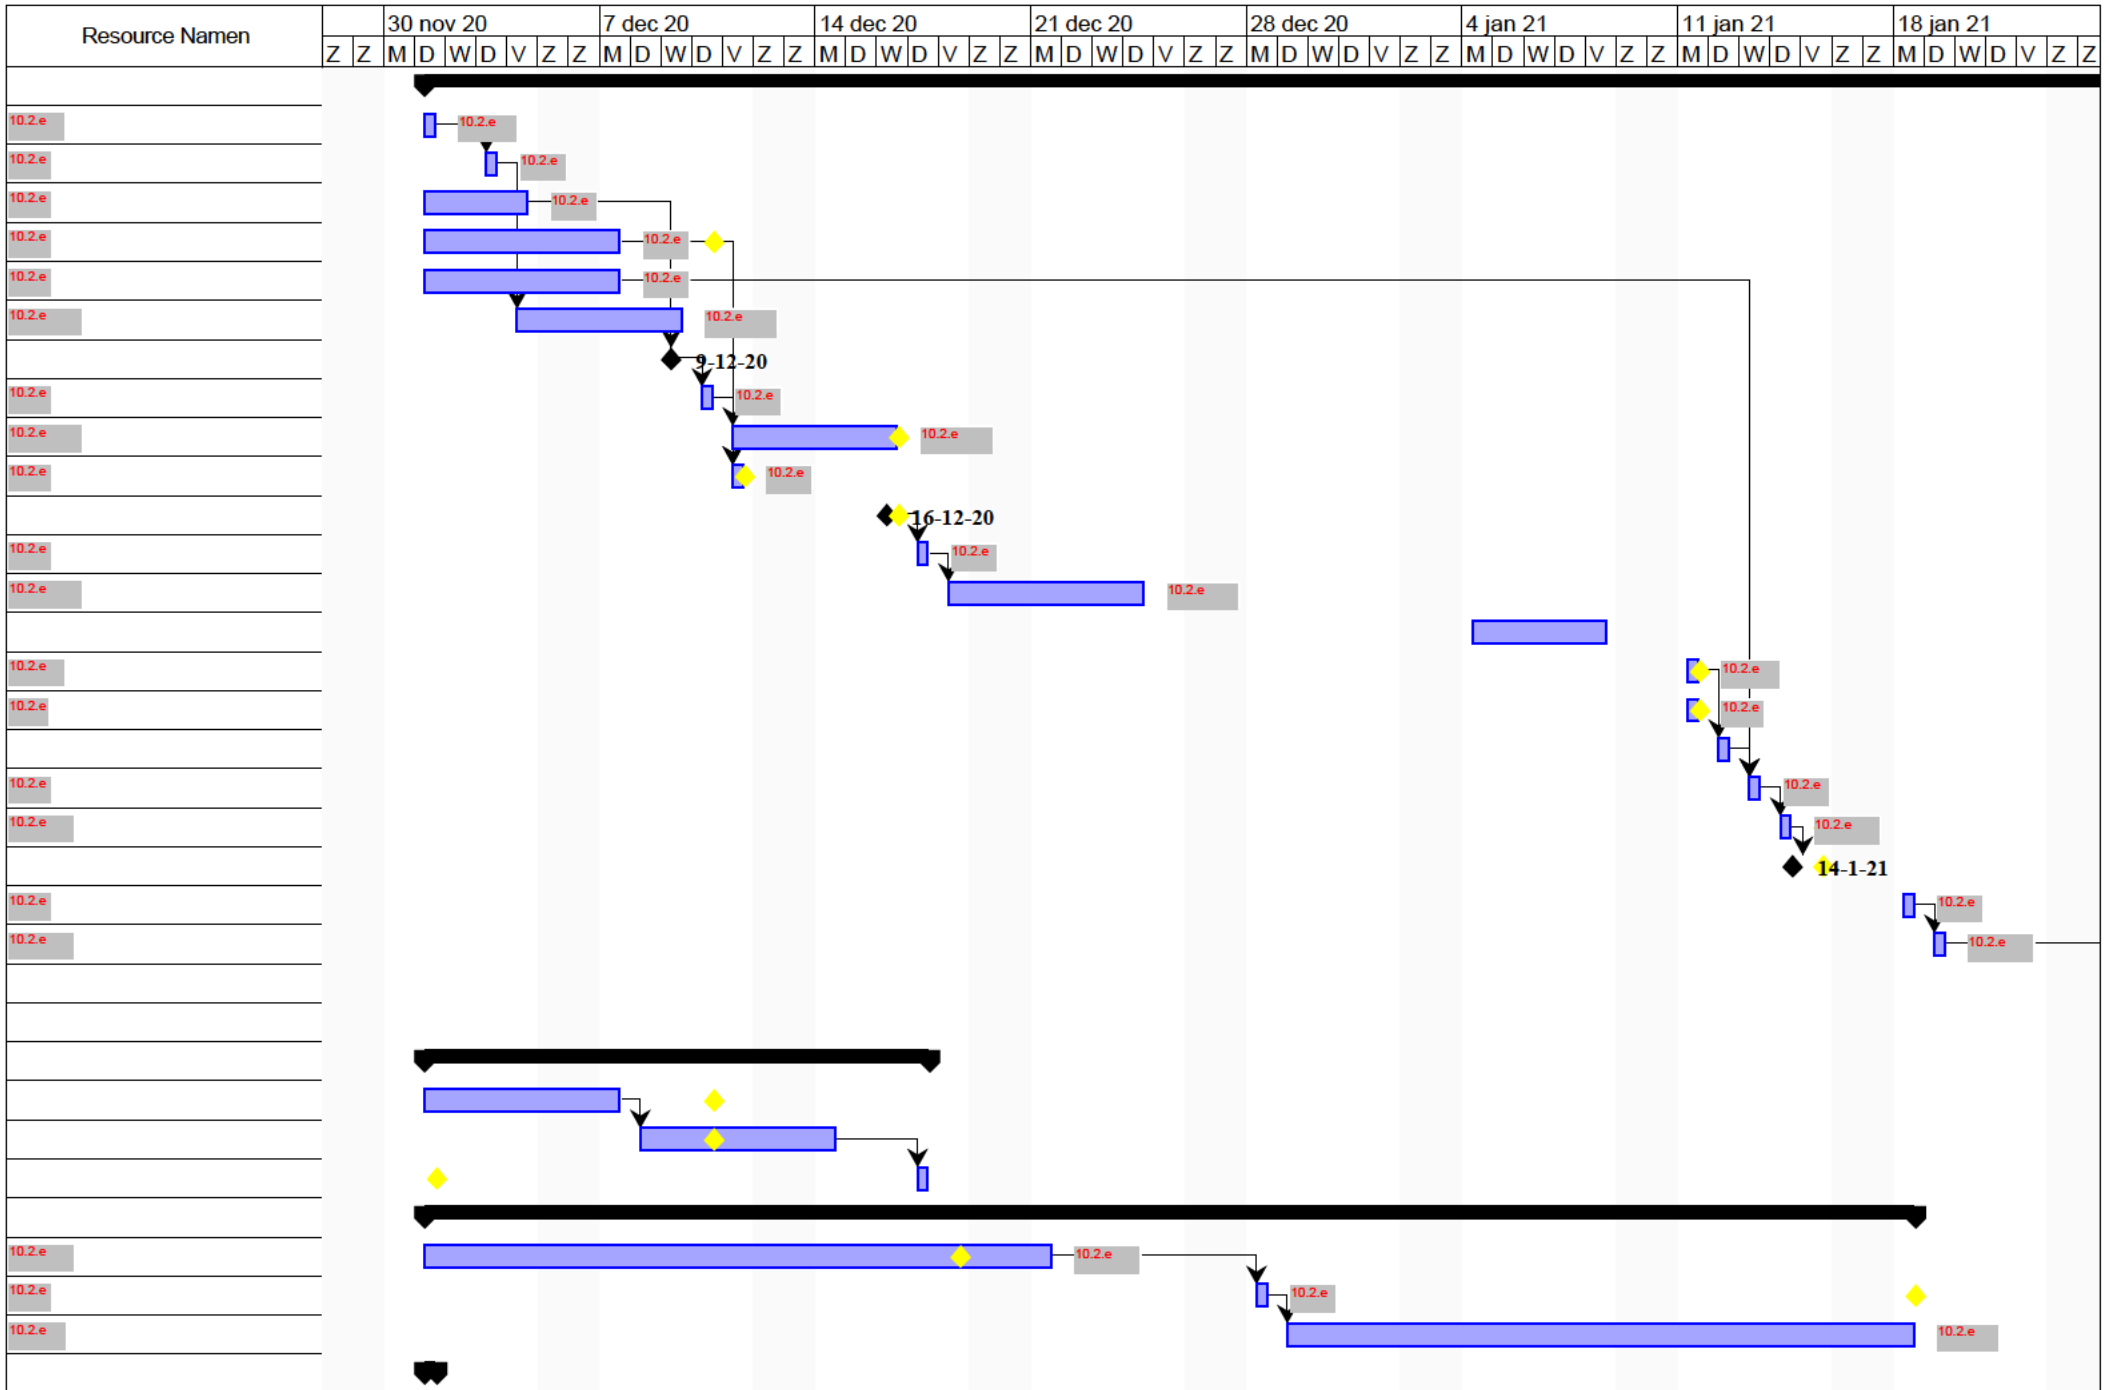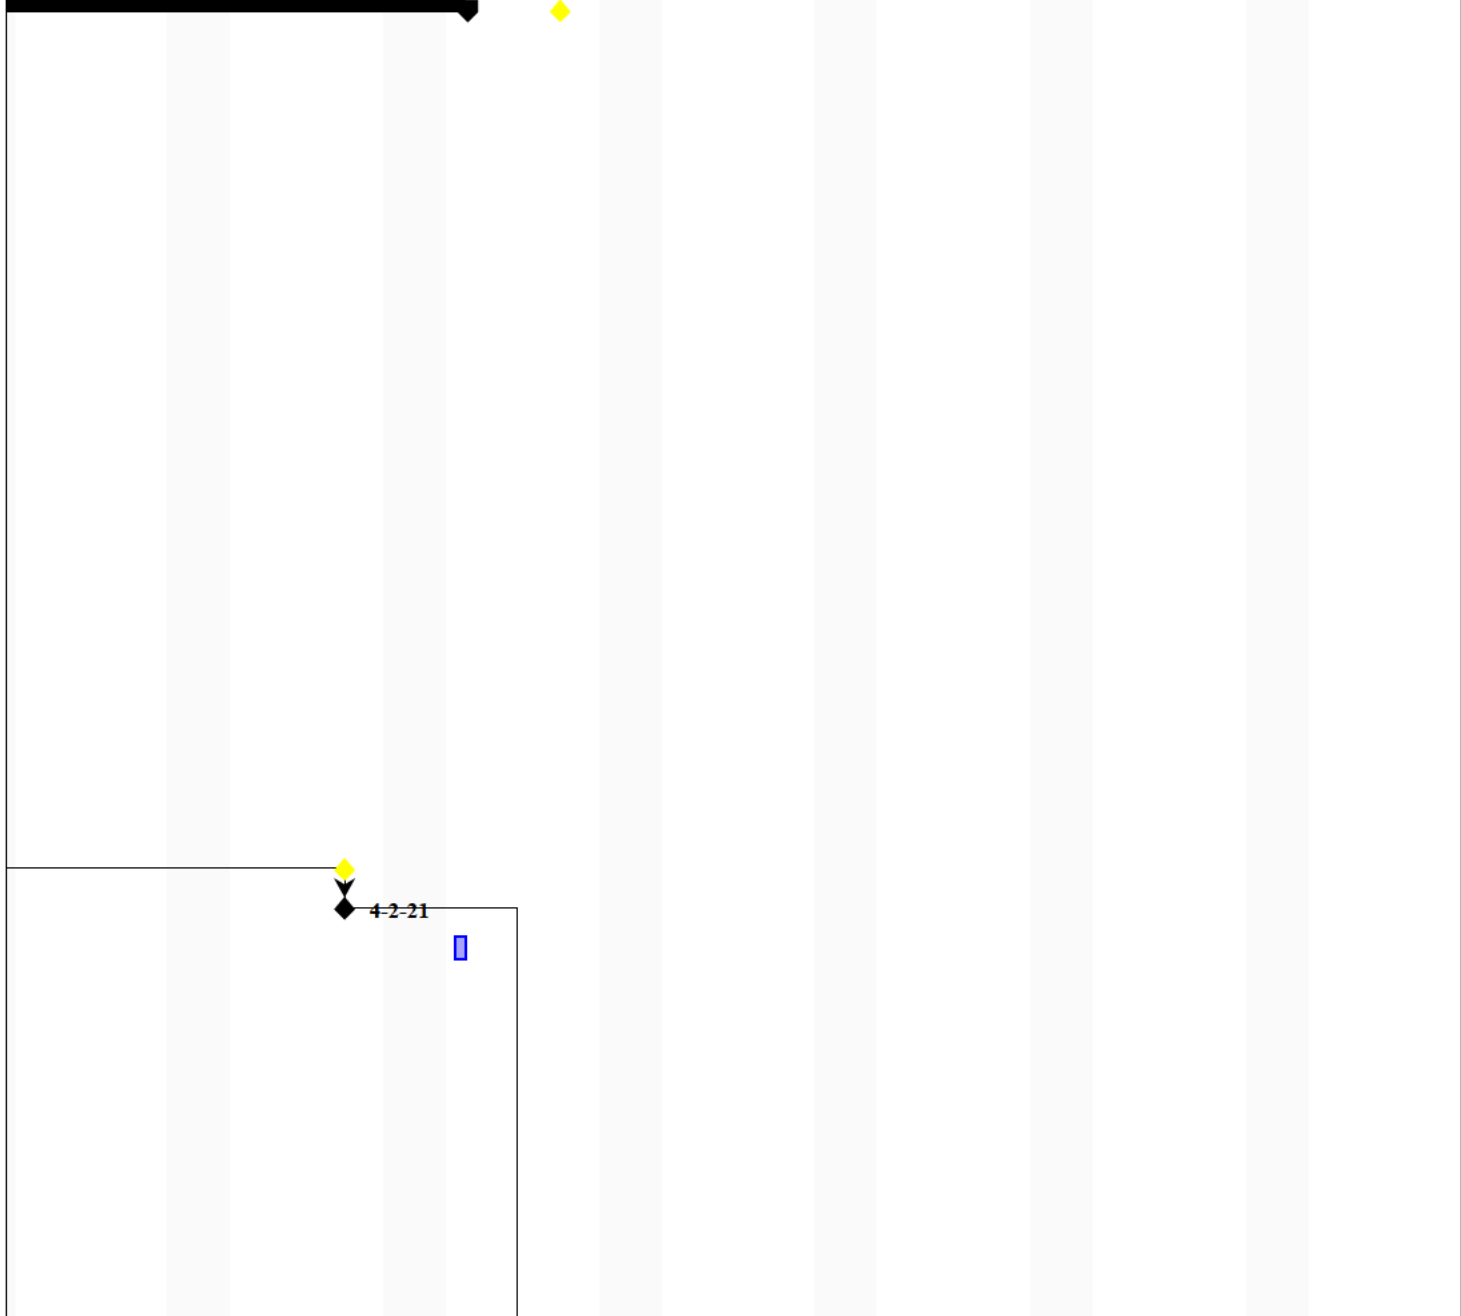

4-2-21

		Naam	Duur	Begin	Einde	Deadline	Voorgangers
35		Aanleveren proces + scr...	1 dag?	1-12-20 8:00	1-12-20 17:00	8-12-20 17:00	
36		Lesmateriaal gereed	10 dagen	2-12-20 8:00	15-12-20 17:00	18-12-20 17:00	35
37		Lesmateriaal getoetst	15 dagen	16-12-20 8:00	5-1-21 17:00	11-1-21 17:00	36
38		Lesmateriaal beschikbaar ...	1 dag?	6-1-21 8:00	6-1-21 17:00	11-1-21 17:00	37
39		Zelfstandig lesmateriaal be...	20 dagen	7-1-21 8:00	3-2-21 17:00		38
40		Communicatie	49 dagen?	4-12-20 8:00	10-2-21 17:00		
41		Communicatie klankbord...	1 dag?	4-12-20 8:00	4-12-20 17:00		
42		Informereren stakeholders	1 dag?	10-2-21 8:00	10-2-21 17:00		24

